A. Construction Works Schedule

Data Date : 28-Jul-25

ACT ID	ACTIVITY DESCRIPTION	Start	Finish	Duration (Cal. Days)
1. Setup / Mobilization				
1	Site Office Setup & Preparation Works (Incl. Temporary Traffic Arrangement (TTA), Permit Application & Approval)	26-Sep-25	14-Dec-26	445
2. Viaduct No.1 - Land Based				
2	Piling, Reinforced Concrete (RC) Works & Other major Work on Viaduct No. 1 (Incl. Testing and Commissioning (T&C))	13-Jan-26	1-Jun-28	871
3. Viaduct No.2 - Marine Based				
3	Piling (at most two marine piles will be constructed concurrently), RC Works & Other major Work on Viaduct No.2 (Incl.T&C)	20-Feb-26	12-May-28	813
3.1	Piles for Bridge Pier 08 (Marine Pile)	19-Sep-26	22-Nov-26	65
3.1.1	Pile for Bridge Pier 08-1 (Marine Pile)	19-Sep-26	9-Oct-26	21
3.1.2	Pile for Bridge Pier 08-2 (Marine Pile)	10-Oct-26	30-Oct-26	21
3.1.3	Pile for Bridge Pier 08-3 (Marine Pile)	31-Oct-26	22-Nov-26	23
3.2	Piles for Bridge Pier 09 (Marine Pile)	10-Jul-26	12-Sep-26	65
3.2.1	Pile for Bridge Pier 09-1 (Marine Pile)	10-Jul-26	31-Jul-26	22
3.2.2	Pile for Bridge Pier 09-2 (Marine Pile)	1-Aug-26	22-Aug-26	22
3.2.3	Pile for Bridge Pier 09-3 (Marine Pile)	23-Aug-26	12-Sep-26	21
3.3	Piles for Bridge Pier 10 (Marine Pile)	26-Apr-26	3-Jul-26	69
3.3.1	Pile for Bridge Pier 10-1 (Marine Pile)	26-Apr-26	20-May-26	25
3.3.2	Pile for Bridge Pier 10-2 (Marine Pile)	22-May-26	12-Jun-26	22
3.3.3	Pile for Bridge Pier 10-3 (Marine Pile)	13-Jun-26	3-Jul-26	21
3.4	Piles for Bridge Pier 11 (Marine Pile)	20-Feb-26	19-Apr-26	59
3.4.1	Pile for Bridge Pier 11-1 (Marine Pile)	20-Feb-26	11-Mar-26	20
3.4.2	Pile for Bridge Pier 11-2 (Marine Pile)	13-Mar-26	25-Mar-26	13
3.4.3	Pile for Bridge Pier 11-3 (Marine Pile)	27-Mar-26	19-Apr-26	24
4. Viaduct No.3 - Land Based				
4	Piling, RC Works & Other major Work on Viaduct No.3 (Incl.T&C)	20-Feb-26	23-Jan-28	703
5. Tung Chung Central Station (TCCS) - Land Based				
5	TCCS Construction (Incl.T&C)	2-Jan-26	15-Nov-28	1049
6. Office & Vehicle Depot (OVD) - Land Based				
6	OVD Building Construction (Incl.T&C)	26-Oct-26	27-Aug-28	672
6.1	Excavation and Leveling related to superstructure	29-Nov-26	27-Aug-27	272
6.2	Underground Utility laying and Remaing Works at Open Space	31-Jul-27	15-Jan-28	169
6.3	North Portion - External Works	16-Nov-26	19-Jun-28	582
7. Seawall Modification - Land Based				
7	Seawall modification works	10-Apr-26	16-Jul-28	829
8. At-Grade Road Work & Promenade - Land Based				
8	Builder workers and uniility installation	5-Mar-27	30-Mar-29	659
9. Statutory Inspection - Land and Marine Based				
9	Statutory Inspection (Obtain Occupation Permit)	3-Sep-28	26-May-29	266

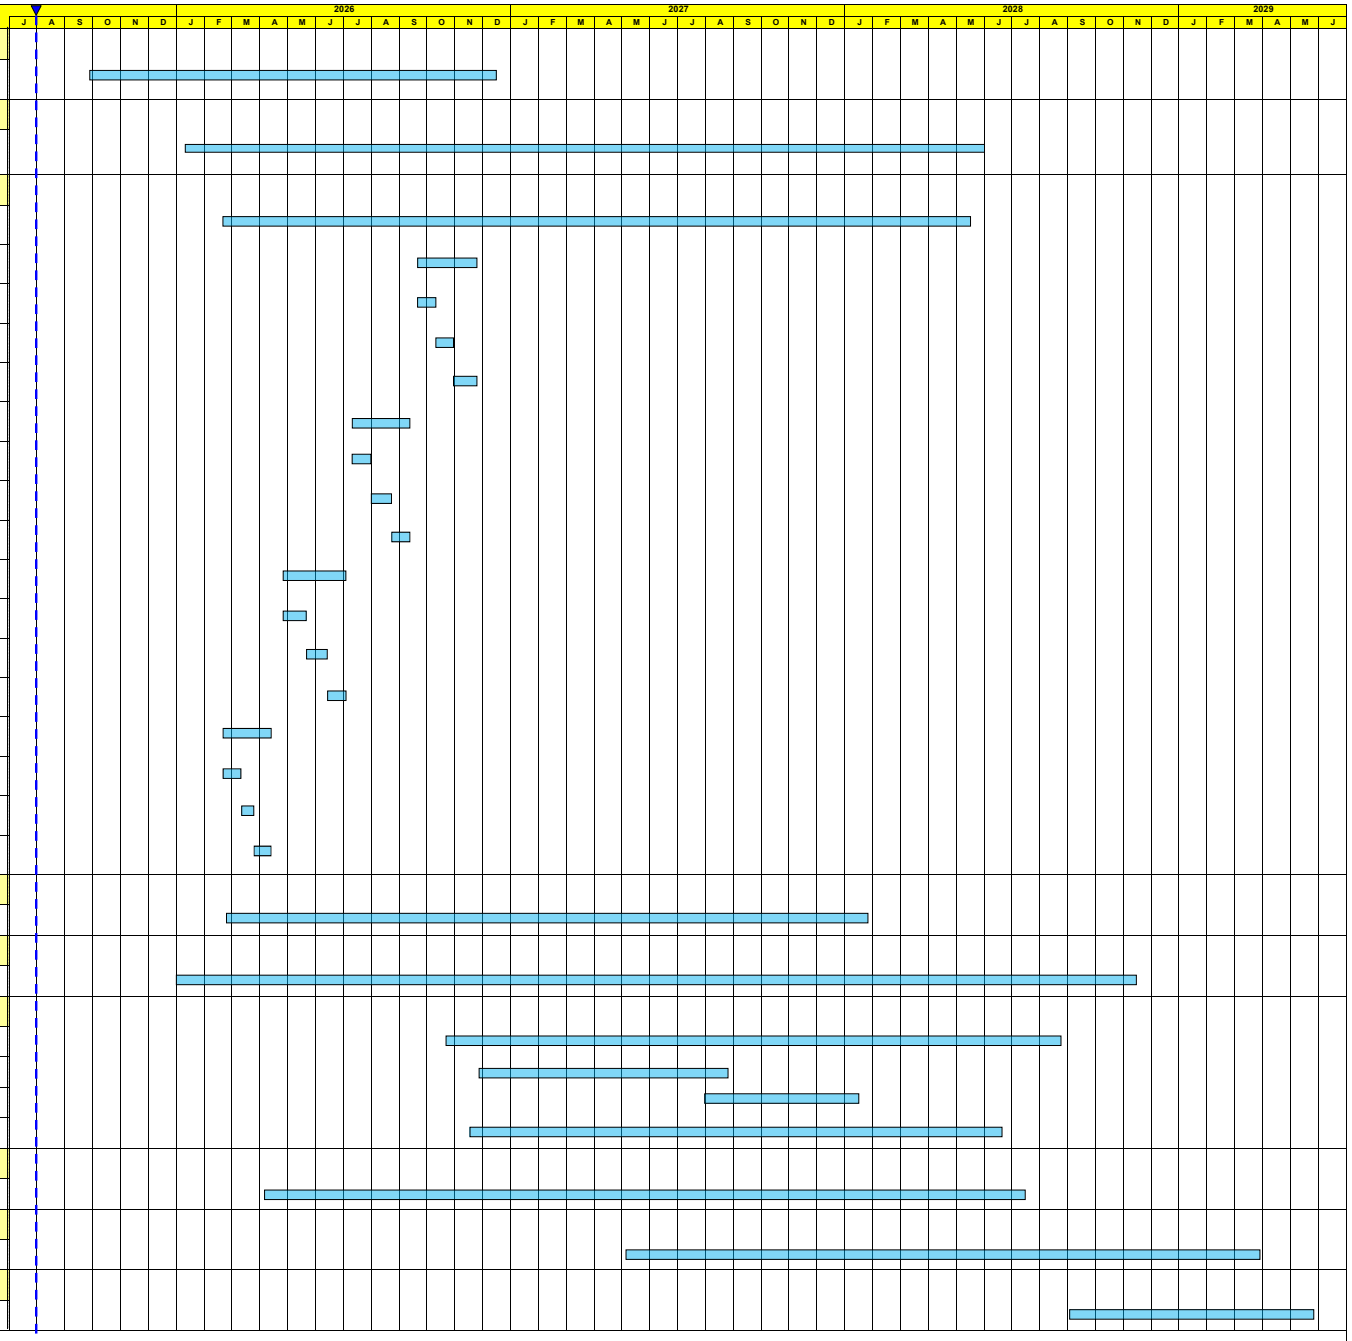

Contract C24W08 - Airport Tung Chung Link
Construction Works Schedule
