
APPENDIX A
CONSTRUCTION PROGRAMME INVOLVING DEPLOYMENT OF SILT CURTAIN

ACT ID	ACTIVITY DESCRIPTION	Start	Finish	Duration (Cal. Days)
Viaduct No.2 Marine Based				
1	Mobilization of plants set up and setting out (include installation of silt curtain and construction of temporary rockfill platform & dismantling of silt curtain and demolition of temporary rockfill platform)	28-Mar-26	7-Jan-27	232
1.1.A	Silt curtain installation at Bridge Pier 8	22-Apr-26	23-Apr-26	2
1.1.B	Silt curtain installation at Bridge Pier 9	2-Oct-26	3-Oct-26	2
1.1.C	Silt curtain installation at Bridge Pier 10	27-Mar-26	28-Mar-26	2
1.2	Silt curtain dismantling on Bridge Pier 8, Bridge Pier 9, Bridge Pier 10 and Bridge Pier 11	7-Jan-27	7-Jan-27	1
1.3	Temporary Rock Fill Platform Construction	23-Jul-26	21-Aug-26	26
1.3.1	Geotextile Laying	23-Jul-26	7-Aug-26	14
1.3.2	Localized silt curtain installation for Bridge Pier 11	8-Aug-26	8-Aug-26	1
1.3.3	Rockfilling Construction	10-Aug-26	21-Aug-26	11
1.4	Temporary Rock Fill Platform Demolition (incl. dismantling of silt curtain)	9-Dec-26	7-Jan-27	26
2	Piling (at most two marine piles will be constructed concurrently, RC Works & Other major Works on Viaduct No.2 incl. T&C)	26-Jun-26	27-Mar-28	627
2.1	Pile for Bridge Pier 08 (Marine Pile)	26-Jun-26	17-Aug-26	60
2.1.1	Pile for Bridge Pier 08-1 (Marine Pile)	26-Jun-26	31-Jul-26	30
2.1.2	Pile for Bridge Pier 08-2 (Marine Pile)	14-Jul-26	17-Aug-26	30
2.2	Pile for Bridge Pier 09 (Marine Pile)	21-Oct-26	15-Dec-26	64
2.2.1	Pile for Bridge Pier 09-1 (Marine Pile)	21-Oct-26	26-Nov-26	32
2.2.2	Pile for Bridge Pier 09-2 (Marine Pile)	27-Nov-26	29-Dec-26	32
2.3	Pile for Bridge Pier 10 (Marine Pile)	20-Aug-26	9-Oct-26	56
2.3.1	Pile for Bridge Pier 10-1 (Marine Pile)	20-Aug-26	21-Sep-26	28
2.3.2	Pile for Bridge Pier 10-2 (Marine Pile)	5-Sep-26	9-Oct-26	28
2.4	Pile for Bridge Pier 11	22-Sep-26	8-Dec-26	64
2.4.1	Pile for Bridge Pier 11-1	22-Sep-26	31-Oct-26	32
2.4.2	Pile for Bridge Pier 11-2	2-Nov-26	8-Dec-26	32

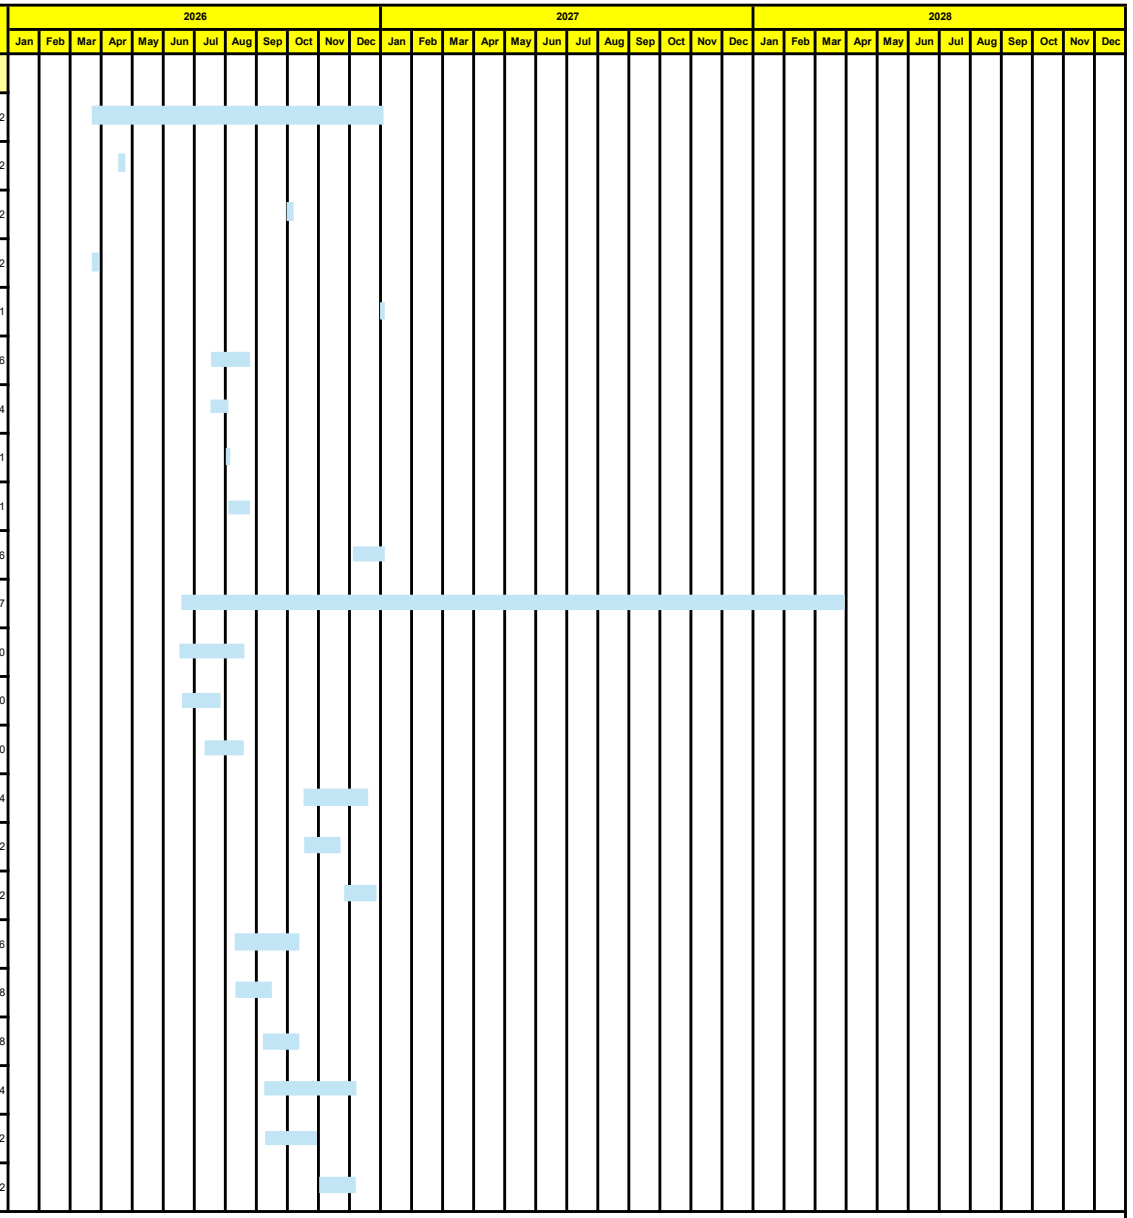

Contract C24W08 - Airport Tung Chung Link

Construction Works Schedule
